



ALEWIFE SEWER SEPARATION PROJECT

Construction Update

December 2014/ January 2015

HURON A

www.cambridgema.gov/theworks/HuronA

DPW Project Manager: Catherine Daly Woodbury

617-349-4818 / cwoodbury@cambridgema.gov

Contractor: P.Gioioso & Sons, Inc.

Upcoming & Current Activity:

- Curb and sidewalk on Larch (N), Standish, Lakeview (S) and Lexington (S), through beginning of Jan 2015, weather permitting.
- Cured in Place Lining activities on Larch (N), Lexington (N) and Lakeview (N) anticipated to be completed in December
- Porous Soil Trench Installation on Grozier (N/S), Lakeview (S), Larch (N), and Lexington (S) to be completed in December.
- Porous Pavement over these trenches will be Spring 2015.
- Curb and sidewalk on Larch (S) and the intersection of Lakeview and Vassal Spring 2015.
- Final Paving on Larch (S), Lexington (S), Lakeview (S) and Standish Spring 2015.
- All remaining plantings areas/bio-basin plantings and tree plantings will resume in Spring 2015.
- **Holiday Schedule:** there will be no construction activity December 25th- January 5th.
- **There will be no construction activity (Huron A only) from mid-Jan to mid-March 2015.**

HURON B

www.cambridgema.gov/theworks/HuronB

DPW Project Manager: Kara Falise

617-349-4827 / kfalise@cambridgema.gov

Contractor: Barletta Heavy Division

Upcoming & Current Activity:

- Miscellaneous drain laterals on Huron Ave, Blakeslee on-going, through December.
- Base paving on Chilton, and Fayerweather (N), is complete.
- Drain and Sewer work on Appleton (Huron to Highland) and is complete.
- Drain and Sewer work on Vassal (Alpine to Reservoir) on-going, through December.
- Temporary pavement overlay on Vassal (Reservoir to Huron) to be completed in December.
- Water work on Fayerweather (Saville to Huron), Granville, and Vassal (Alpine to Reservoir) is complete.
- **Holiday Schedule:** there will be no construction activity December 20th- January 5th.

CONCORD

www.cambridgema.gov/theworks/ConcordArea

DPW Project Manager: Catherine Daly Woodbury

617-349-4818 / cwoodbury@cambridgema.gov


Contractor: P.Gioioso & Sons, Inc.

Upcoming & Current Activity:

- Water, sewer, drain on Corporal Burns, Fayerweather and Copley is complete.
- Test pits on Baystate, Field, and Garden on-going through January.
- Water, sewer and drain work on Alpine (between Vassal and Field) through January.
- Sewer and drain work on Walden (Garden to Concord) to be completed early December.
- Water, sewer, and drain work on Birch anticipated to start in January.
- **Holiday Schedule:** there will be no construction activity December 25th- January 5th.



Construction Progress

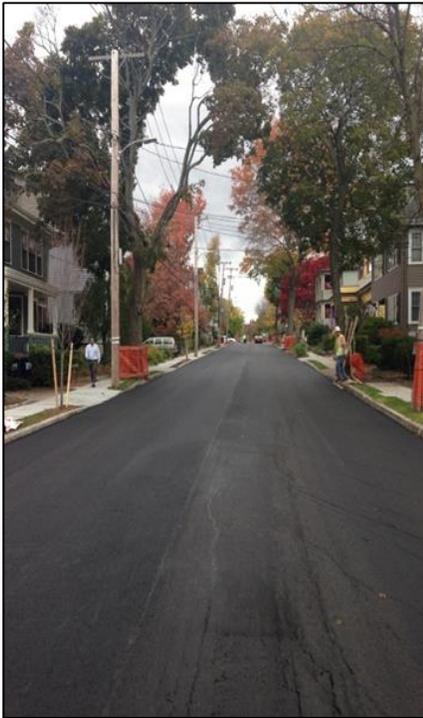

Huron A- Road with completed sidewalks and final paving.




Drain and sewer on Fayerweather St.



Paving on Grozier Rd.

Shop and be Merry!

Support Local businesses while holiday shopping during the **Huron Village Annual Holiday Stroll** on **Thursday, December 11th from 6:00- 8:00 pm**. Enjoy special discounts, snacks, drinks, and music. Experience what Huron Village shops and restaurants have to offer!



Follow them on Facebook:

www.facebook.com/huronvillage

www.facebook.com/ObservatoryHill

Contact

For any project questions or to be placed on a project specific mailing list, contact KyAnn Anderson of Kleinfelder, the City's Community Relations Manager at kanderson@kleinfelder.com / 617-498-4708.

Department of Public Works After-Hours Emergency Hotline: (617)349-4800



www.cambridgema.gov/TheWorks

