FOUNDATIONS AREA DEFINITIONS

CONCRETE SEQUENCING

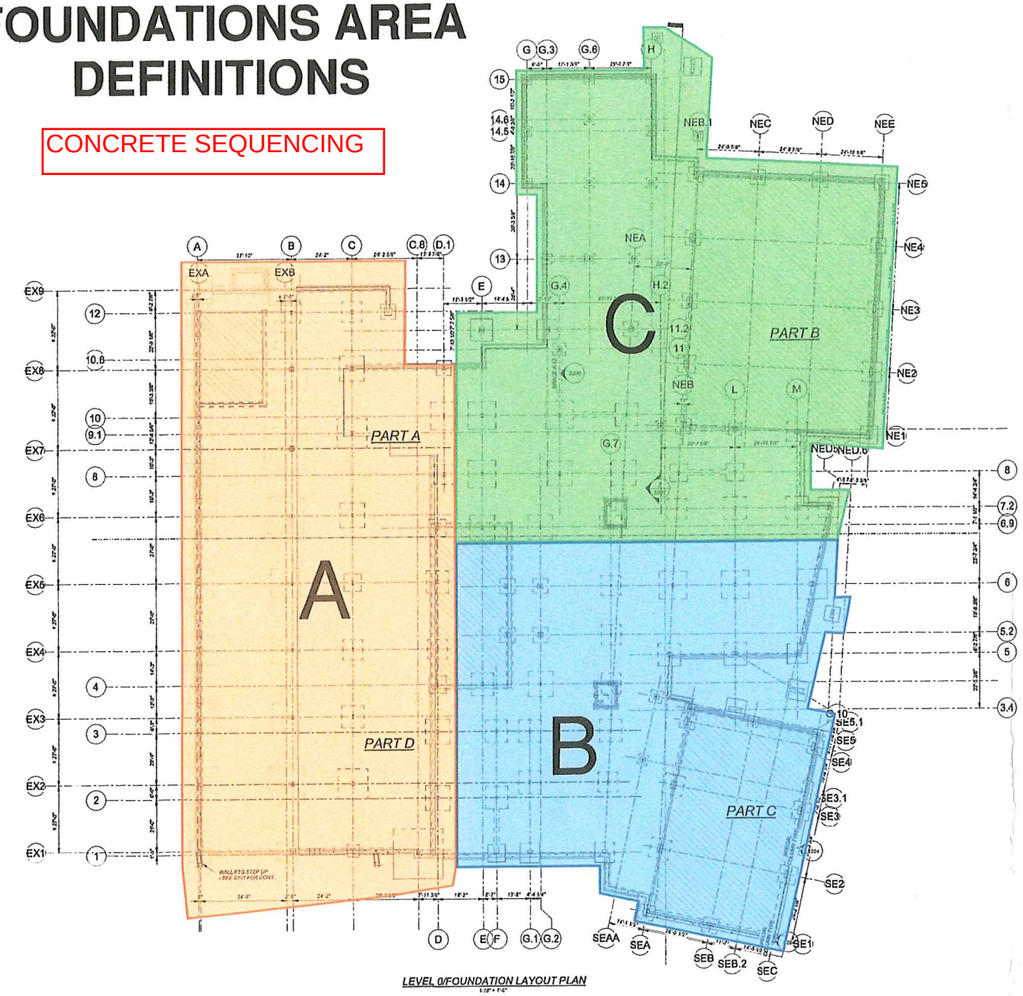

STRUCTURAL STEEL AREA DEFINITIONS

STEEL SEQUENCING

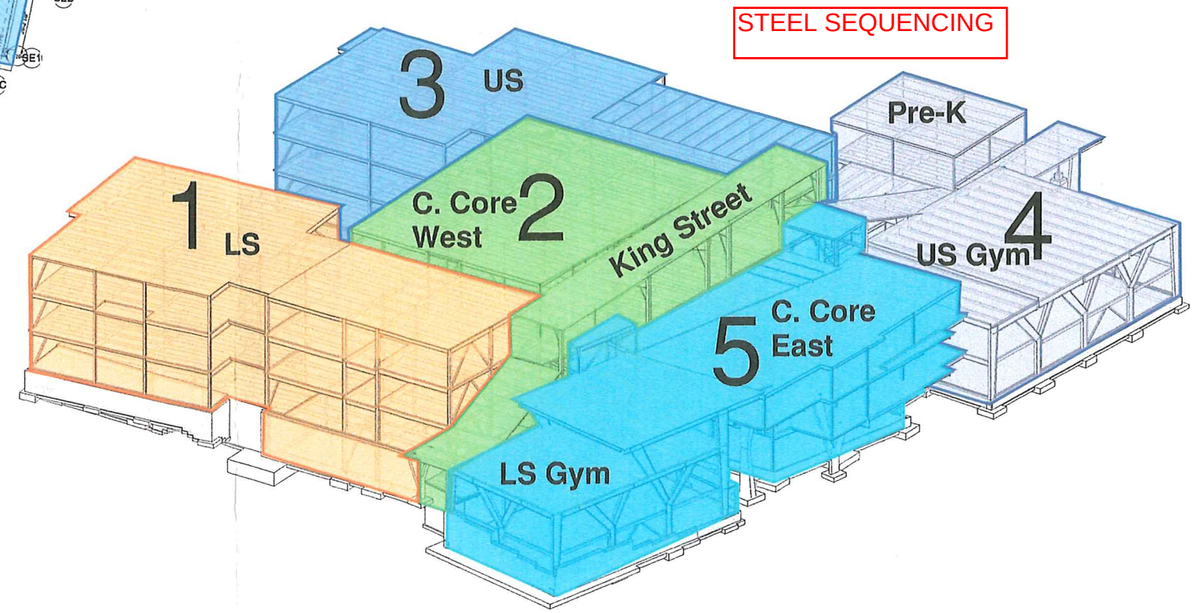

As of 5/30/14

MLK School

Look Ahead Schedule

		SUNDAY	MONDAY	TUESDAY	WEDNESDAY	THURSDAY	FRIDAY	SATURDAY
This Coming Week	DATE	**25-May**	**26-May**	**27-May**	**28-May**	**29-May**	**30-May**	**31-May**
	TASKS		Backfill Geothermal Hayes St. Area B, C Fnds - Excavation, Formwork, Backfill Commence with Steel Area 1	Backfill Geothermal Hayes St. Area B, C Fnds - Excavation, Formwork, Backfill Commence with Steel Area 1	Backfill Geothermal Hayes St. Area B, C Fnds - Excavation, Formwork, Backfill Commence with Steel Area 1	Backfill Geothermal Hayes St. Area B, C Fnds - Excavation, Formwork, Backfill Commence with Steel Area 1	Backfill Geothermal Hayes St. Area B, C Fnds - Excavation, Formwork, Backfill Commence with Steel Area 1	Work Tenative
Week 1	DATE	**1-Jun**	**2-Jun**	**3-Jun**	**4-Jun**	**5-Jun**	**6-Jun**	**7-Jun**
	TASKS		Area B, C Fnds - Excavation, Formwork, Backfill Steel Area 1 Soil Trucking	Area B, C Fnds - Excavation, Formwork, Backfill Steel Area 1 Soil Trucking	Area B, C Fnds - Excavation, Formwork, Backfill Steel Area 1 Soil Trucking	Area B, C Fnds - Excavation, Formwork, Backfill Steel Area 1	Area B, C Fnds - Excavation, Formwork, Backfill Steel Area 1	Work Tenative
Week 2	DATE	**8-Jun**	**9-Jun**	**10-Jun**	**11-Jun**	**12-Jun**	**13-Jun**	**14-Jun**
	TASKS		Area B, C Fnds - Excavation, Formwork, Backfill Steel Area 1 Commence with Geothermal Drilling Kinnaird St.	Area B, C Fnds - Excavation, Formwork, Backfill Steel Area 1 Commence with Geothermal Drilling Kinnaird St.	Area B, C Fnds - Excavation, Formwork, Backfill Steel Area 1 Commence with Geothermal Drilling Kinnaird St.	Area B, C Fnds - Excavation, Formwork, Backfill Steel Area 1 Commence with Geothermal Drilling Kinnaird St.	Area B, C Fnds - Excavation, Formwork, Backfill Steel Area 1 Commence with Geothermal Drilling Kinnaird St.	Work Tenative
Week 3	DATE	**15-Jun**	**16-Jun**	**17-Jun**	**18-Jun**	**19-Jun**	**20-Jun**	**21-Jun**
	TASKS		Area B, C Fnds - Excavation, Formwork, Backfill Steel Area 1 Geothermal Drill Kinnaird Commence with Kinnaird Utility Structures	Area B, C Fnds - Excavation, Formwork, Backfill Steel Area 1 Geothermal Drill Kinnaird Commence with Kinnaird Utility Structures	Area B, C Fnds - Excavation, Formwork, Backfill Steel Area 1 Geothermal Drill Kinnaird Commence with Kinnaird Utility Structures	Area B, C Fnds - Excavation, Formwork, Backfill Steel Area 1 Geothermal Drill Kinnaird Commence with Kinnaird Utility Structures	Area B, C Fnds - Excavation, Formwork, Backfill Steel Area 1 Geothermal Drill Kinnaird Commence with Kinnaird Utility Structures	Work Tenative
